



FMD Implementation Status Report

Country: *Czech Republic*

Responsible personnel: *[Pavla Štisová, Project Manager]*

Date: *[January 18th, 2018]*

Overall country readiness: *[On the same level as Mainstream]*

This report covers project status and provides all necessary information regarding current status of FMD implementation in Czech Republic monitoring progress of both Governance Work Stream in form of Czech Medicines Verification Organization (CZMVO-NOOL) and Technical Work Stream in form of National Medicines Verification System (NMVS). Additionally, the report provides current status of Legal environment.

Contents

FMD Implementation Status Report	1
Contents	1
Project plan and timeline	2
Governance Work Stream (CZMVO-NOOL).....	2
A-1) Implement national stakeholder organization	3
Technical Work Stream (NMVS).....	4
B-2) System testing and qualification.....	5
B-3) Go-live and Ramp up to full operation with all users connected	9
B-4) Pharmacies and hospitals Readiness	10
B-5) Manufacturers and Parallel Distributors Readiness (in common „MAH“)	11
B-6) Wholesalers Readiness	12
Legal Work Stream	13
Status of FMD project in the Czech Republic compare to other countries	14
Number of MAHs, which uploaded data to NSOL =CZMVS successfully	16
Number of uploaded products and packs	16

Project plan and timeline

Overall initial project setup status:



Step	Status
A steering group to take overall accountability, provide support, resources and budgets set up and working	[Done]
A project manager who is in overall charge of the implementation process assigned and working	[Done]
A project plan with clear milestones and work-packages created and approved	[Done - detail project plan and other documents updated together with the IT supplier and approved by NOOL board]
A project team to carry out the activities organized in work streams set up and working	[Done]

Governance Work Stream (CZMVO-NOOL)

Overall work stream status:



Step	Status
Alignment between all Stakeholders	[Done]
Memorandum of Understanding (MoU) signed	[Done]
CZMVO-NOOL Statutes agreed	[Done]
CZMVO-NOOL established	[Done – 6.3.2017 registered]

Additional remarks:

[Web pages <http://czmvo.cz/> were established. Update of the project status is provided regularly]



A-1) Implement national stakeholder organization

Step status:

Relevant topics	Status
CZMVO-NOOL entered into contracts with IT service providers	[Done – Solidsoft Reply has been chosen, contract signed by June 2017]
CZMVO-NOOL entered into contract with EMVO	[Done – EMVO contract was approved by NOOL board and signed by both countries]
CZMVO-NOOL set up a relationship with national competent authorities (NCA)	[Done – NOOL continues in cooperation with NCAs – intensive cooperation with SÚKL during WS, seminars, answers to the questions from the market; activities will continue]
CZMVO-NOOL created contract with end-users	[Done – contract was approved by NOOL board]
CZMVO-NOOL entered into contracts with end-users in pilot	[Done – contract send to pilot participants, start of signing the contract NOOL from 16.4.2018, 100% of pilot participants signed the contract]
CZMVO-NOOL entered into contracts with end-users	[In progress – from 24 th October registration and connecting of end-users including signing the Agreement on the use of the NOOL National is published for information on web pages www.czmvo.cz , 1829 companies till now were invited to begin registration, 1185 signed the contract with NOOL, 1124 companies with their localities =pharmacies and warehouses are created and connected to NSOL=CZMVS]
CZMVO-NOOL created contract for MAHs and NOOL	[Done – comments to contract proposal for MAH adopted and approved by board; MAHs to be informed during May 2018; information regarding registration process published on web www.czmvo.cz by end of May]
CZMVO-NOOL entered into contracts with MAHs	[In progress – Contract proposal for MAH presented on the web pages as a part of registration process with NOOL from end of May 2018; 283 MAHs signed contract with NOOL already, 338 MAHs registered]



Relevant topics	Status
CZMVO-NOOL defined the fees for MAHs related to NSOL for 2019	[Done – fees approved by NOOL board, model “flat fee”- according to the EMVO’s recommendation registration fee + annual user fee; MAHs informed and information regarding registration process published on web www.czmvo.cz in May; fee reduction for small MAHs was approved for user fee 2019 -communication published by 30 th August 2018 on web pages NOOL]
CZMVO-NOOL received requests for reduced user fee for 2019, signed contract amendment	[In progress – requests for reduced user fee received and being processed, applications can be sent till 30 th January 2019, contract Amendment approved by NOOL board, communication directly to applicants will follow]

Additional remarks: [N/A]

Technical Work Stream (NMVS)

Overall work stream status:



B-1) System implementation support

Step	Status
IT service provider selected, cooperation started	[Done - regular weekly calls between Solidsoft Reply and NOOL and together with access to Confluence database to share documentation; a control visit to Solidsoft Reply took place from 16 th -17 th October]
Quality Assurance (QA) over technical and project part of implementation performed on the ongoing basis	[Done – cooperation with EY continues; continuous process revision related to FMD a quality system preparation for NOOL]
Technical workshops were done between Solidsoft and IT providers to pharmacies and distributors; all requirements to modify systems are known to IT providers of end user systems	[Done – WS with IT providers were prepared by NOOL & Solidsoft; WS took place on 30.8. and 20.9 and 30.11., communication regarding IT WS and registration of IT SW companies described on web www.czmvo.cz , including agenda and NDAs proposals]
Fully functional registration portal for end-users of	[Done – registration process and contract signature



Step	Status
NMVS is in place	with end-user was set by NOOL; registration portal being tested and modified with pilot participants, registration of all end-users started by 24 th October 2018 in the phases step-by-step]
Fully functional registration portal for MAHs, which sell/markets medicinal products on the Czech market	[Done – registration process and contract signature with MAHS was published by NOOL on web pages - ; www.czmvo.cz/cs/uzivatele-systemu/registracni-proces/ ; by 14 th December 326 MAHs registered, registration continues; all necessary information available on the web page]

Additional remarks:

[N/A]

B-2) System testing and qualification

Step status:

Relevant topics	Status
ITE (Integrated testing environment) available and accessible	[Done – testing environment accessible by all IT suppliers providing distribution and pharmacy SW registered with Solidsoft after they attended IT WS; testing started]
Communication for pilot participants in place	[Done – NOOL presented the communication regarding participation in pilot on www.czmvo.cz ; memorandum of cooperation is signed with registered pilot participants - 52 pilot participants applied; registration closed; introductory meeting with pilot participants was realised, individual meetings with pilot producers and IT SW companies continues, further communication with all pilot participants via teleconf. + via freedcamp aps.]
Pilot phase planned in detail	[Done – NOOL in cooperation with Solidsoft, EY and Expert group prepares detail plan of the pilot phase, check-list of readiness for pilot, contact list of participants, test scenarios etc.]
Kick-off meeting with pilot participants realised	[Done – NOOL prepares the meeting of pilot participants; kick-off meeting 9.1.2018]
Testing prepared and planned	[Done – NOOL together with IT group of Solidsoft customers defined automated testing – 2000 tests; testing strategy and ITAT and UAT test plan for



Relevant topics	Status
	verification approved]
ITAT (integration acceptance testing) of NSOL done	[Done – ITAT of NSOL successfully done 8.-12.1.2018, mainly automated testing (2000 tests) for all Solidsoft Reply customers, additional ITAT for R 1.1 was realised 1 st week in March 2018]
1. Part of validation QMS NOOL by EMVO successfully completed	[Done – required QMS documentation was provided to EMVO, revised documents and additional requirements for updates from EMVO provided back; statement of successful validation was provided]
2. Part of validation QMS NOOL by EMVO successfully completed	[Done – required QMS documentation was provided to EMVO, validation closed and passed on 23 rd April 2018 by positive report from EMVO]
Process of validation and contract acceptance between NOOL and end-users in place and tested	[Done – NOOL portal for verification and contract approval with end-users was tested as well as Solidsoft Reply portal for companies' registration and creating of access credentials to CZMVS; the manual was updated and published on NOOL web pages, also presented on webinar by ČLnK regarding the process of end-users connecting to CZMVS]
IQE (Integrated quality environment) available and accessible	[Done – IQE available for IT SW companies – pilot participants for self-certification]
UAT (user acceptance testing) done and approved validation criteria achieved	[Done – user acceptance testing of Solidsoft Reply blueprint system took place in Ljubljana in Slovenia 19.-25. January managed by NMVO Slovenia - ZAPAS. Full end-to-end testing of the system took place using pack data uploaded by 2 producers to the EU Hub and with the 2D data matrix codes scanned using Slovenian pharmacy and wholesaler IT systems. The testing took place in the EU Hub and Solidsoft Reply national blueprint system quality environments which are identical to the relevant live production environments.
UAT 1.3 (user acceptance testing) for Release 1.1 was done and validation criteria approved	[Done – according to EMVO new requirements for additional functionalities „Master data update“ for EU HUBu & NMVS before pilot starts extra UAT 1.3 for Release 1.1 done 20.3.2018; same approach lead by ZAPAZ Slovenia]
NMVS tested (including security, individual interfaces including interface to European Hub, UAT – user acceptance testing, OAT etc.)	[Done – UAT took place during 4th week in January 2018 in Slovenia – ZAPAS together with other Solidsoft Reply customers, additional UAT 1.3. for R 1.1 successfully realised on 20.3., OAT provided



Relevant topics	Status
	during following weeks]
NMVS test results review	[Done – ITAT test report available, UAT test report 1.3. for R 1.1 reviewed and approved by NOOL and EMVO]
Self-certification of “end-users’ IT systems” started	[In progress –started in IQE; self-certification of end-user IT systems readiness is a mandatory condition together with end-user contract/conditions acceptance to be connected to the NMVS; Guide material available in Confluence, 231 IT SW companies passed validation with their SW till now for connecting to CZMVS]
Information to public about pilot testing preparation	[Done – 13.3.2018 press conference organized by NOOL took place; few pilot participants as well as SÚKL and MZ ČR representatives attended press conference about pilot of FMD project, 10.4.2018 stakeholder meeting on british embassy with Solidsoft Reply, stakeholders representatives and pilot participants with MZ ČR, SÚKL and NOOL]
Technical „go-live“	[Done – connection between NMVS PRD and EU HUB PRD after successful UAT 1.3. for R 1.1. and passing documentation validation part 2 by EMVO from 25th April 2018]
Pilot test with selected producers, hospital, distributor and pharmacies was done	[Done – start of pilot phase May 3rd 2018, duration until last planned release of new functionalities in Autumn 2018, run in the production environment; producers/MAHs willing to up-load the data for serialized products during pilot should contact NOOL via info@czmvo.cz , pilot will continue till the end of this year]
Data for medicinal products uploaded successfully to NMVS	[Done – up to 14 th December product data to medicinal products uploaded by 90 MAHs – currently in CZMVS 4 669 673 medicinal products, uploaded batches numbers available in NOOL and IT SW companies]
All end-users participating in the pilot connected to CZMVS	[Done – based on signature of end-user contracts and IT systems certification pilot participants were connected]
First product successfully verified in pharmacy/hospital	[Done – during pilot – on 28 th June 2018 – hospital pharmacy FN Sv. Anny Brno successfully verified and supplied first medicinal product (uploaded by Roche



Relevant topics	Status
	company in EU HUB for CZMVS. Verification with support of SW Farmis]
Products verified in pharmacies/hospitals in the pilot	[Done – hospital pharmacies, 2 pharmacy chains, group of 4 pharmacies, distributors]
Feedback from pilot and findings corrections/change proposals	[In progress – continuous communication with all pilot participants regarding system functionalities, registration portal and other related items; relevant findings and recommendations from the pilot to be shared outside the pilot as well; correction of bugs and findings related to CZMVS to be done during R 4.1.]
ITAT – integrated testing – NSOL R 2.0 as well as documentation review for release R 2.0 completed	[Done – ITAT successfully done 7.-13.6.2018, automated tests, all Solidsoft Reply customers, Documentation review complete]
UAT 2.0 (user acceptance testing) for Release 2.0 was done	[Done – successfully passed on 21st June, all Solidsoft Reply customers; data provided by Johnson and Johnson (J&J); 12 end-to-end test cases; Production environment Release 3.7.2018]
ITAT – integrated testing – NSOL R 3.0 as well as documentation review for release R 3.0 completed	[Done – ITAT successfully done 23.-30.8.2018, automated tests, all Solidsoft Reply customers, Documentation review complete, 100% of planned test done, 99% successfully passed, no failures priority 1 or 2]
UAT 3.0 (user acceptance testing) for Release 3.0 was done	[Done – successfully passed on 20th September, all Solidsoft Reply customers; data provided by Johnson and Johnson (J&J); 26 end-to-end test cases; Production environment Release 2.10.2018.]
ITAT – integrated testing – NSOL R 4.0 as well as documentation review for release R 4.0 completed	[Done – ITAT successfully done 8.-13.11.2018, automated tests, all Solidsoft Reply customers, documentation under revision now]
UAT 4.0 (user acceptance testing) for Release 4.0 was done	[Done – successfully passed on 26 th November, all Solidsoft Reply customers; data provided by J&J; 27 end-to-end test cases in Zapas and Danish systems; Production environment Release 6.12.2018]
ITAT – integrated testing – NSOL R 4.1 as well as documentation review for release R 4.1 completed	[In progress – minor release planned for 30th January]
End-to-end testing of komplex EMVS system	[In progress – 4 countries are part of testing – 2 with Solidsoft Reply systems (Czech Republic and



Relevant topics	Status
completed	Denmark) 2 with Arvato systems (Norway and France), preparation of test scenarios, tests to be provided after 4.1. release]
All requirements on the IT solution met	[In progress – validation of the system is compared to User Requirement Specifications = URS]

Additional remarks:

[UAT = User Acceptance testing; IQE = Integrated Quality Environment; OAT = Operation Acceptance testing]

B-3) Go-live and Ramp up to full operation with all users connected

Step status:

Relevant topics	Status
Go-Live date set up	[Done –connection between NMVS PRD and EU HUB PRD date “technical go-live” from 25 th April 2018; ramp-up start during Q4]
Go-live and post-go-live support prepared	[In progress – monitoring preparation started, preparation of support for alerts handling]
Go-Live QA performed	[In progress –continuously from beginning of the pilot phase in production environment; QMS documentation reviewed and completed]
NMVS up and running	[In progress – functionalities added in releases of the system]
QMS audit of Solidsoft Reply	[Done– scope agreed and approved, external auditor selected, audit took place on 8-10 th January 2019; no critical or high findings were identified; closer report should be provided to SSR and its customers by 25 th January, CAPA plan should follow]
ISMS audit NSOL	[In progress – scope definition and RFP, external auditor selected, audit takes place from 3rd-22nd January 2019; no critical or high findings were identified till now]

Additional remarks:

[N/A]

B-4) Pharmacies and hospitals Readiness

Step status:

Relevant topics	Status
Pharmacy SW providers fully informed	[Done – NOOL provides information to with end users during seminars and also by publishing information on web www.czmvo.cz and other web pages, workshops with hospital representatives on 29.9., 31.10. a 23.11.; presentations and video from WS is available on the web pages; instructions how to register into Confluence and NOOL published on web NOOL; informative IT WS took place on 9th October 2018 with presence of IT SW companies representatives, SÚKL, NOOL]
Pharmacy SW providers fully trained and educated	[Done – 3 WS with IT providers were prepared by NOOL & Solidsoft; info regarding IT WS is available in - WS agenda, NDA, presentation and video (access based on requirement for companies with signed NDA); pilot finding regarding IT systems + connection of end-users from system point of view was presented to IT SW companies during informative IT WS on 9th October 2018 with presence of IT SW companies representatives, SÚKL, NOOL; all IT companies were provided by access to freedcamp]
IT SW adjustment and connection to NMVS implemented and tested by pharmacy SW providers	[In progress – ITE used, IQE started to be used for self-certification by IT companies; 22 IT SWs for pharmacies and distributors validated by 14th December]
Pharmacies fully informed	[In progress – NOOL organized workshops with hospitals and pharmacies on 26.9., 31.10. and 23.11., information provided to webs and portals www.nemlek.cz a www.apatykar.cz ; manuals how to connect, is on NOOL web side https://www.czmvo.cz/cs/uzivatele-systemu/lekarnici/ (English version to be provided soon) and for use by ČLnK for trainings and webinars on 8.11 and 15.11.2018 – can be seen on ČLnK web pages]
Pharmacies fully trained and educated	[In progress – in pilot, recommendations to other subjects to be provided on web pages or via seminars' stakeholders' responsibility to train their members]
Pharmacies connected to NMVS and tested by	[In progress – 992 companies with their localities



Relevant topics	Status
pharmacies	(pharmacies) are connected to CZMVS now]
Pharmacies ready for go-live	[In progress]

Additional remarks:

[N/A]

B-5) Manufacturers and Parallel Distributors Readiness (in common „MAH“)

Step status:

Relevant topics	Status
MAH SW providers fully informed	[Done – NOOL started information process with manufactures during seminar on 2nd July and via AIFP and ČAFF associations; also by publishing information on web CZMVO; regular information provided by associations AIFP, ČAFF; information materials for MAHs under preparation as well as WebEx meetings and workshops in Q1/2018]; information meeting for pharmaceutical companies regarding EMVO on-boarding requirements and FMD with EMVO, SÚKL and NOOL representatives realised on 10 th April 2018 in SÚKL premises – video with presentation published on NOOL web; info for MAHs available on EMVO web: https://emvo-medicines.eu]
MAH SW providers fully trained and educated	[Done- info regarding IT related to MAH is available https://emvo-medicines.eu/]
MAHs fully informed	[In progress – NOOL provides information via AIFP and ČAFF associations; also by publishing information materials on web CZMVO; under preparation materials regarding contracts and fee system published on web www.czmvo.cz https://www.czmvo.cz/en/system-users/registration-process/]
MAH s fully trained and educated	[In progress – all info regarding MAHs on-boarding on EMVO www.emvo-medicines.eu in „Knowledge Database“, news also on www.czmvo.cz]
EMVS implemented and tested by MAHs	[Done– MAHs or OBPs connect to EU HUB and upload data for serialized product, data used for testing by end users connected]



Relevant topics	Status
MAHs ready for go-live	[In progress]

Additional remarks: [On – boarding to EU HUB should be done as soon as possible as this seems to be critical risk in terms of time planning and readiness]; OBP = onboarding partner]

B-6) Wholesalers Readiness


Step status:

Relevant topics	Status
Wholesaler SW providers fully informed	[Done – NOOL providing information to wholesalers during seminars and also by publishing information on web www.czmvo.cz]
Wholesaler SW providers fully trained and educated	[Done - WS with IT providers were prepared by NOOL & Solidsoft; info regarding IT WS is available – WS agenda, NDA, presentation and video (access based on requirement for companies with signed NDA)]
NMVS implemented and tested by wholesaler SW providers	[Done – in pilot]
Wholesalers fully informed	[In progress – NOOL providing information to wholesalers by publishing information on web www.czmvo.cz]
Wholesalers fully trained and educated	[In progress – in pilot]
Wholesalers connected to NMVS and tested by wholesalers	[In progress – 132 distribution companies with their warehouses are connected now]
Wholesalers ready for go-live	[In progress]

Additional remarks: [N/A].

Legal Work Stream

Overall work stream status:

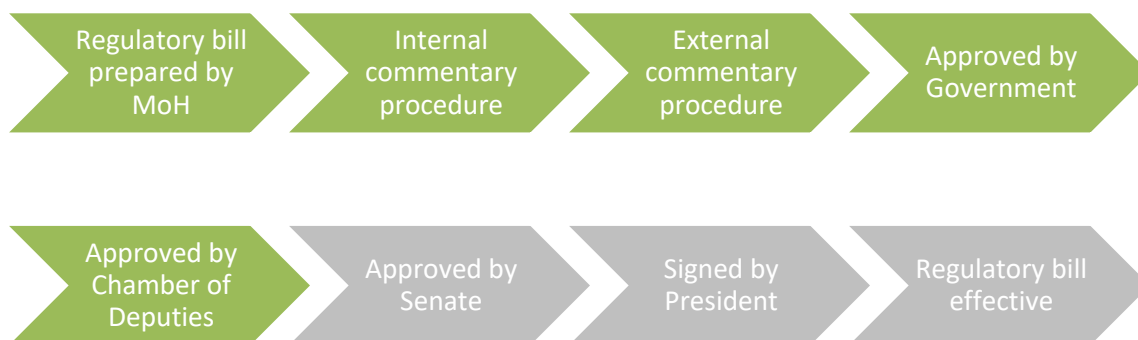

Step	Status
Regulatory bill prepared by MoH	[Done – The amendment to the Pharmaceuticals Act prepared by Ministry of Health and send for comments – till 1 st March 2018]
Internal commentary procedure	[Done – comments sent by relevant subjects; processed by Ministry of Health]
External commentary procedure	[Done – subjects provided their comments during May]
Approved by Government	[Done – approved by Government and pass to the Chamber of Deputies of the Parliament of the Czech Republic]
Approved by Chamber of Deputies	[Done -The amendment to the Pharmaceuticals Act passed / was approved in the Chamber of Deputies of the Parliament]
Approved by Senate	[In progress – to be discussed during week from 21 st January]
Signed by President	[Not yet]
Regulatory bill effective	[Not yet]



Additional remarks: [N/A]



Status of FMD project in the Czech Republic compare to other countries

(EMVO reporting – December 2018 report)

EXECUTIVE SUMMARY A1: MAH ON-BOARDING *

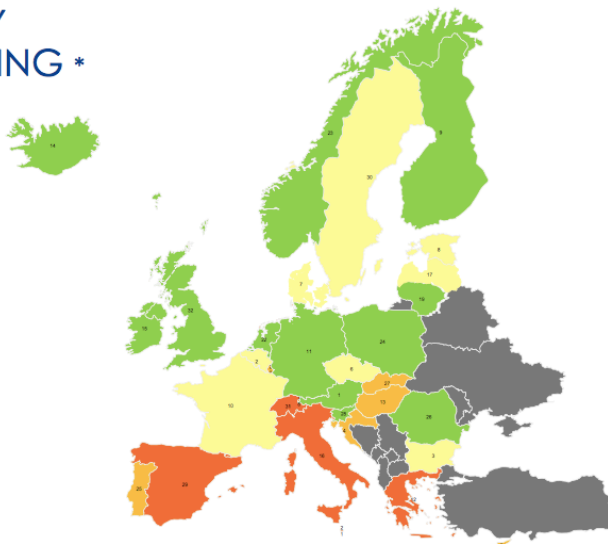



* Does not imply to be connected to the EU Hub

PMMR 2.1 DEC 2018

emvo European Medicines
Verification Organisation

25

EXECUTIVE SUMMARY A2: NMVS READINESS

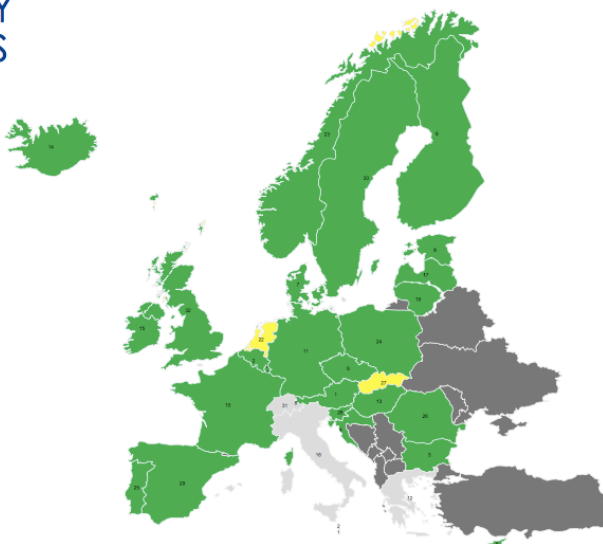



PMMR 2.1 DEC 2018

emvo European Medicines
Verification Organisation

26



EXECUTIVE SUMMARY A3: END USER READINESS

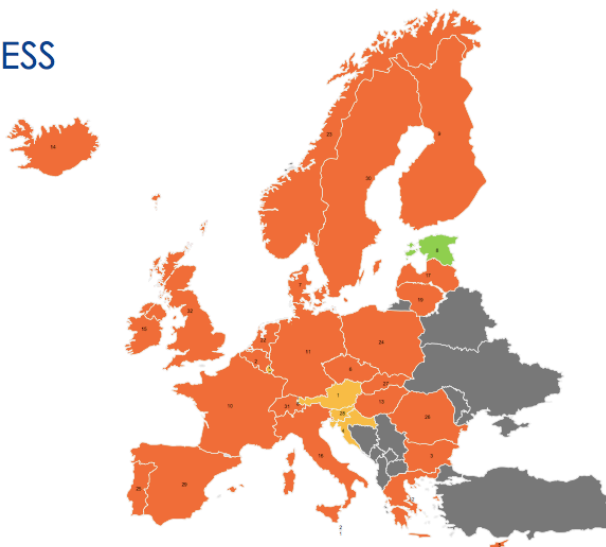


PMMR 2.1 DEC 2018

emvo European Medicines Verification Organisation

27

NMVO ON-BOARDING - PROGRESS OVERVIEW

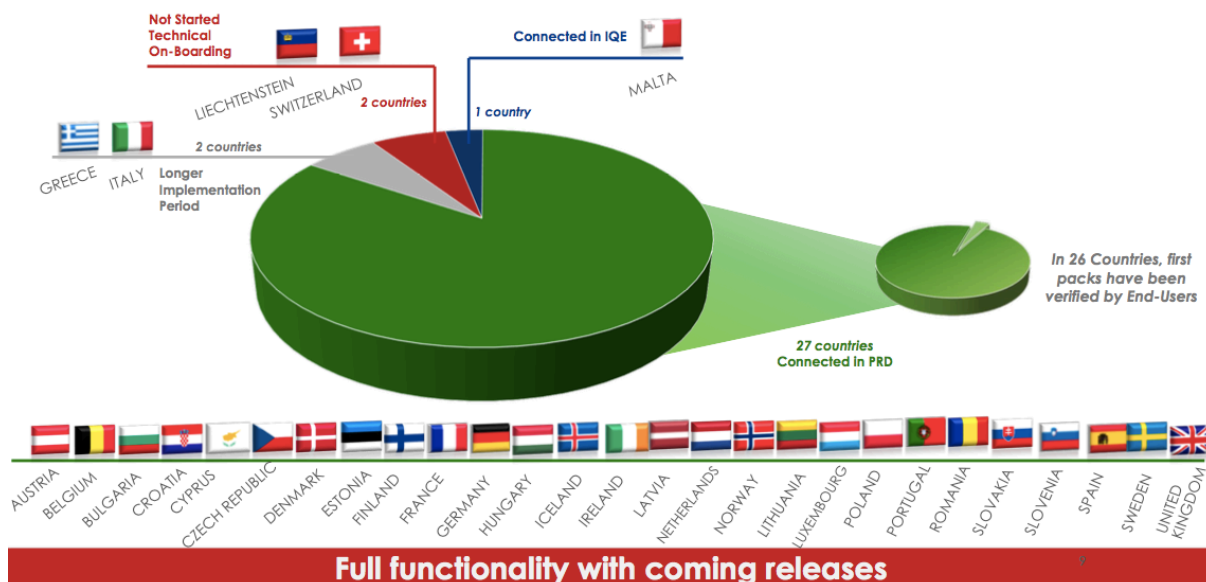


Explanation of abbreviations:

- A1 - Alarm 1 MAH On-Boarding
- A2 - Alarm 2 NMVS Readiness



- A3 - Alarm 3 End User Readiness – not measured yet
- CH - Connected to Hub
- EC - End User Connected
- FP - First Packs verified
- Fund - NOOL Funding secured
- PS - Products Serialized Uploaded
- PC - Pilot successfully completed
- SY - End User System Connected
- Tasks - NOOL Initial Tasks complete
- Team - NOOL Team implemented
- TIS - Technical Implementation started

Number of MAHs, which uploaded data to NSOL =CZMVS successfully

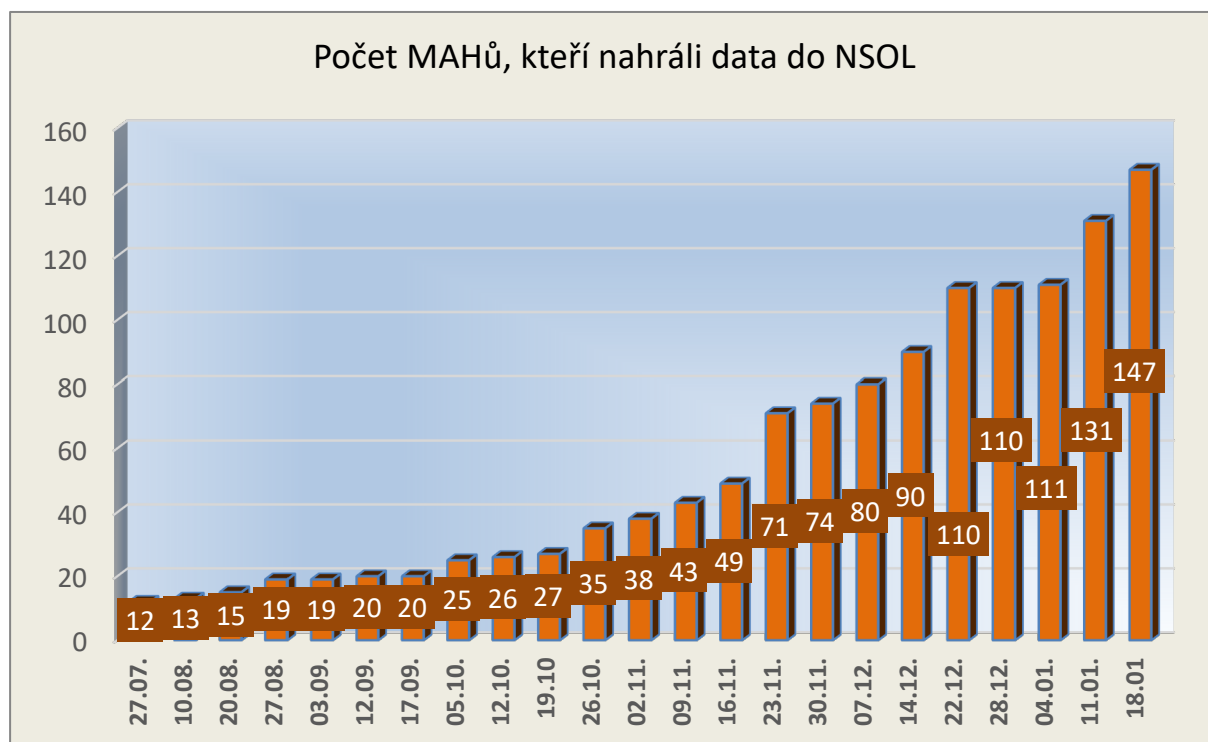

Number of uploaded products and packs

